Oak Ridge Elementary School Construction Status Report

Date – 10 December 2004

Schedule: Status Compared to Contract A

Description	Rem Dur	Early Start	Early Finish
Kitchen, Dining - Area B	83	06/07/04	03/23/05
Administration - Area C	83	05/18/04	03/23/05
Kindergarten - 1st Grade wing - Area G	83	05/12/04	03/23/05
4th - 5th Grade wing - Area F	144	05/20/04	06/16/05
2nd - 3rd Grade wing - Area E	150	06/21/04	06/24/05
Renovation of Media Center Area D	70	03/31/05	07/06/05
Gym/Stage Area A	75	06/06/05	09/16/05

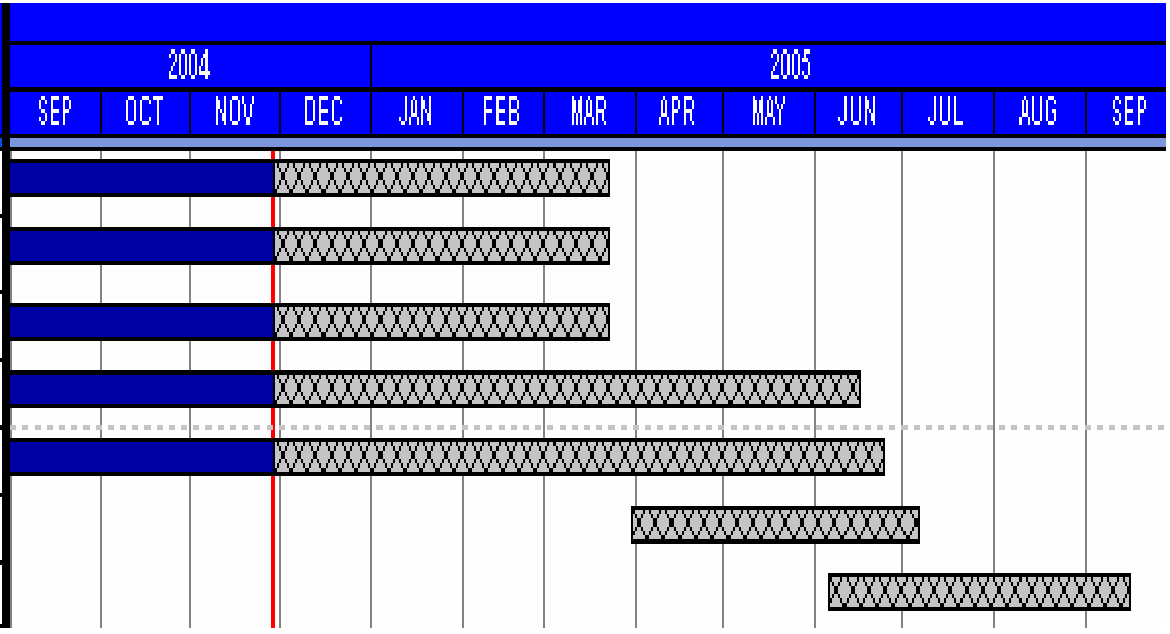

Working Issues

- Widening of NC 150 (GCS, NC DOT)
- Ball Field Lighting (GCS)
- Abatement plan (GCS, HICAPS)
- School sign (HICAPS, CG&A, GC)

2 Week Recap

- HVAC equipment in Area B.
- Brick of Area G.
- CMU in Areas B, C, E, F & G.
- Windows started in Area G.
- HVAC equipment in Area G Mezzanine
- Floor in Area C/D.
- Drywall in Mezzanine Area G

2 Week Look Ahead

- Installation of Brick Area B.
- Metal Roof on Area G.
- Installation of Windows in Area G.
- Concrete walks at Canopy 1 & 2.
- Metal stud walls on Area C.
- Canopy 1 & 2 steel and roof decking
- Student rerouting to support concrete pour at canopies
